
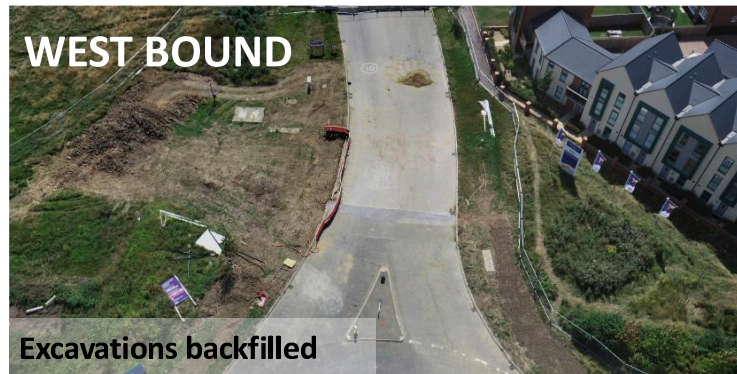
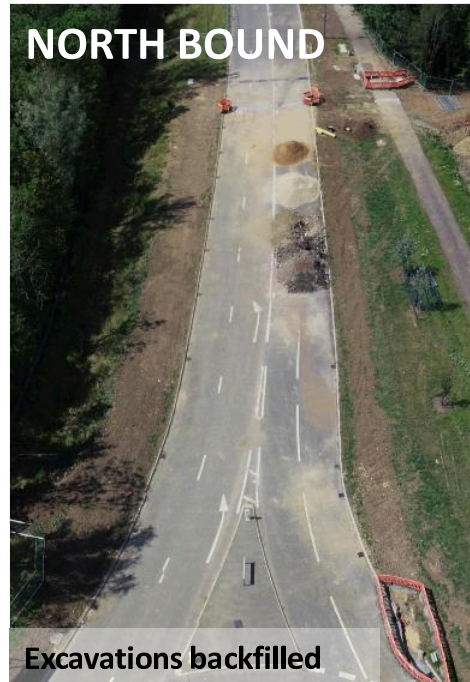


WHITEHOUSE UNDERPASS UPDATE

WEEK COMMENCING JULY 29TH 2019

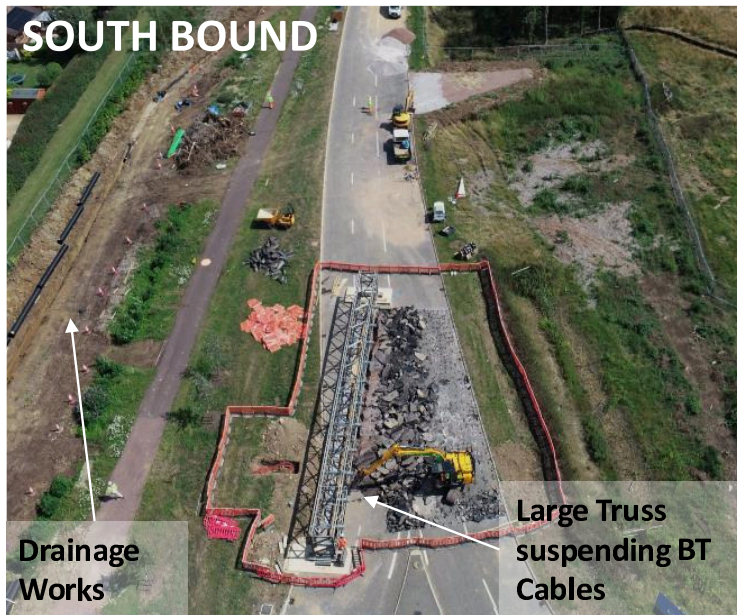

Progress Update

5 of the 6 utilities have successfully been diverted to date. The remaining will continue over the next couple of weekends

Now the diversion works have primarily been completed the priority is backfilling the holes dug for the utilities and start the temporary works to allow the excavation for the underpass.

As part of the temporary works there are 12 fibre BT ducts which aren't being diverted due to the cost, but instead suspended. A large, 26m long truss has been placed into position by a 150T crane. This was a very careful lift that requires lots of people and resources to ensure the truss is safely lifted into position. The photo in the middle shows the truss in place with straps holding the BT cables in place. This will stay here until early 2020 when the underpass has been put in underneath it

There are also drainage works happening on site which couldn't previously be installed due to the clash with the utilities, because the utilities have now been diverted this drainage can now be installed.

A construction access will be created to the North of Whitehouse Roundabout to enable construction traffic to access the roundabout and continue with other works while major excavation is taking place to the south. This is for V4 Whitehouse Roundabout construction traffic only.

Works happening over the next couple of weeks

Commencement of excavation for underpass construction, and continue drainage works



WORKING TOGETHER TO IMPROVE OUR HIGHWAY

Follow us @Ringway_MK

Submit feedback

Comment on our site, submit a question about our services.



Visit www.mkhighways.co.uk to provide feedback
